

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Blood Bank Inventory & Emergency Donor Matcher

Name: Harish Ramesh Kumar SRN: PES1UG24AM111 Section: B Date: 02 October 2026

1. Epics and User Stories (Backlog)

My Lab 1 requirements (5 functional and 2 non-functional) were grouped into 4 Epics: Emergency Request Management (BBDM-1), Donor Matching & Notification (BBDM-2), Blood Inventory Management (BBDM-3) and Donor Profile & Data Privacy (BBDM-4). These were broken into 14 User Stories worth 63 story points. Each story is written as “As a / I want / So that”, linked to its parent Epic, and ranked by priority (10 High, 3 Medium, 1 Low).

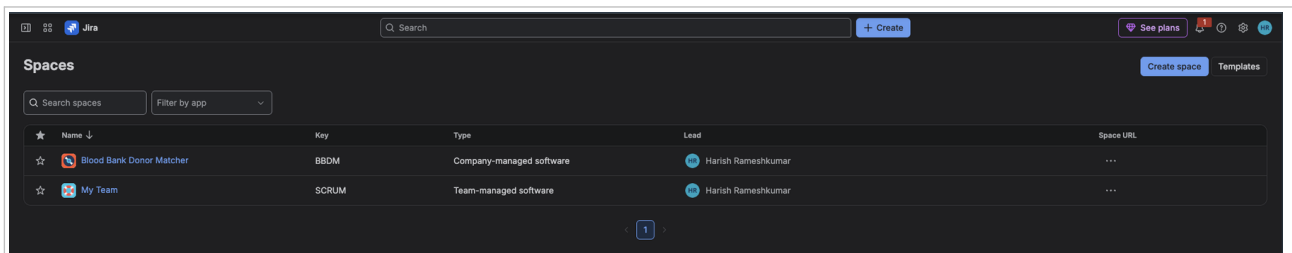


Figure 1: Jira space Blood Bank Donor Matcher (key BBDM, company-managed software)

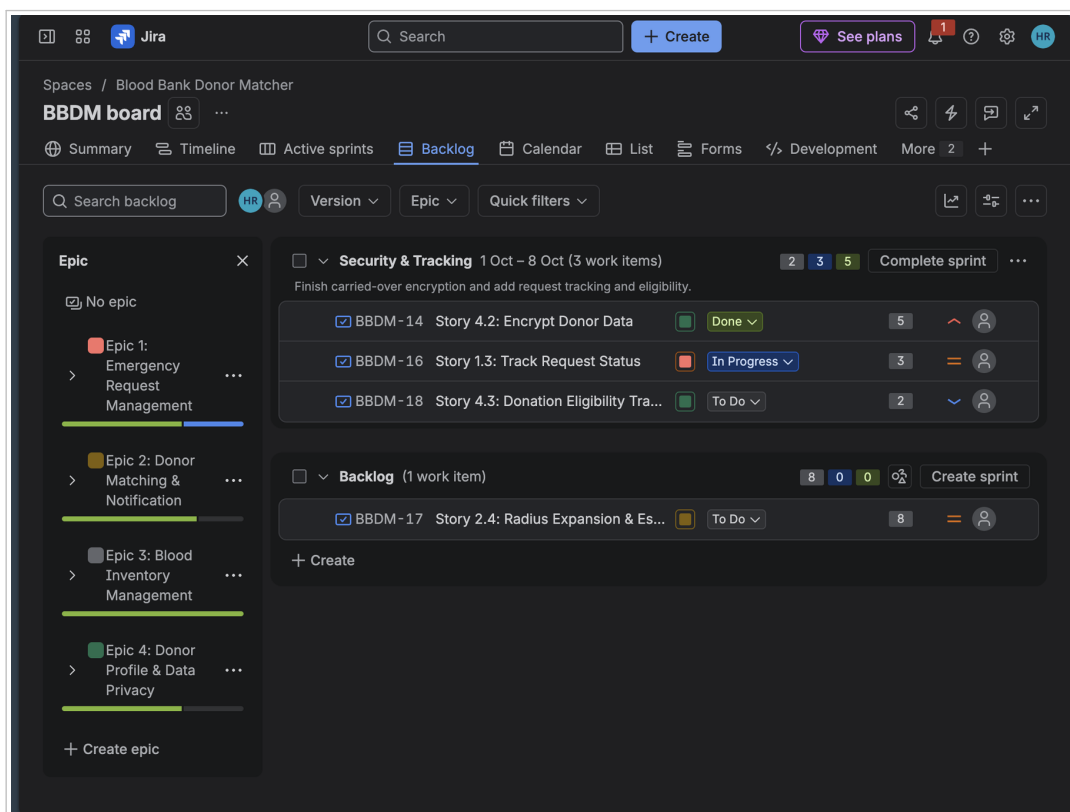


Figure 2: Backlog with the Epic panel open, showing all four Epics with their progress bars

Work	Assignee	Reporter	Priority	Status	Resolution	Created	Updated	Due date
BBDM-1 Epic 1: Emergency Request Management	Unassigned	Harish Rameshk...	Medium	To Do	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:09	None
BBDM-7 Story 1.1: Submit Emergency Request	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:13	None
BBDM-13 Story 1.2: Urgency Triage	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:16	None
BBDM-16 Story 1.3: Track Request Status	Unassigned	Harish Rameshk...	Medium	In Progress	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:24	None
BBDM-2 Epic 2: Donor Matching & Notification	Unassigned	Harish Rameshk...	Medium	To Do	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:09	None
BBDM-10 Story 2.1: ABO/Rh Compatibility Check	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:13	None
BBDM-11 Story 2.2: Geo-targeted SMS Alerts	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:16	None
BBDM-12 Story 2.3: Donor Confirm/Decline	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:16	None
BBDM-17 Story 2.4: Radius Expansion & Escalation	Unassigned	Harish Rameshk...	Medium	To Do	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:09	None
BBDM-3 Epic 3: Blood Inventory Management	Unassigned	Harish Rameshk...	Medium	To Do	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:09	None
BBDM-5 Story 3.1: Update Stock	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:12	None
BBDM-8 Story 3.2: Real-time Availability Check	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:13	None
BBDM-9 Story 3.4: Prevent Double Allocation	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:13	None
BBDM-15 Story 3.3: Expiry Flags	Unassigned	Harish Rameshk...	Medium	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:16	None
BBDM-4 Epic 4: Donor Profile & Data Privacy	Unassigned	Harish Rameshk...	Medium	To Do	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:09	None
BBDM-6 Story 4.1: Register/Update Donor Profile	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:13	None
BBDM-14 Story 4.2: Encrypt Donor Data	Unassigned	Harish Rameshk...	High	Done	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:24	None
BBDM-18 Story 4.3: Donation Eligibility Tracking	Unassigned	Harish Rameshk...	Low	To Do	Unresolved	01 Oct 2026, 12:09	01 Oct 2026, 12:23	None

Figure 3: List view: all 14 User Stories grouped under their four Epics, with priority and status

2. Story Point Assignments and Sprint Planning

Story points were assigned using Fibonacci values (2, 3, 5, 8), sized relative to a reference story (Story 3.1, Update Stock, at 3 points) and adjusted for complexity and uncertainty, following Planning Poker principles. Three one-week sprints were planned with dependencies first: inventory, donor profiles and compatibility logic before alerts and escalation.

Sprint	Stories	Planned	Outcome
Sprint 1 Foundation	3.1, 4.1, 1.1, 3.2, 3.4, 2.1	26 pts	26 completed
Sprint 2 Alerts & Monitoring	2.2, 2.3, 1.2, 3.3, 4.2	24 pts	19 completed; 4.2 (5 pts) carried over
Sprint 3 Security & Tracking	4.2 (carried over), 1.3, 4.3	10 pts	Active: 5 completed so far

Story 2.4 (Radius Expansion & Escalation, 8 points) stays in the backlog for a future sprint. Total backlog size is 63 points (Epic 1: 11, Epic 2: 26, Epic 3: 16, Epic 4: 10).

BBDM board					
Ask AI Search work Filter Group					
	Work	Priority	Status	Parent	Story Points
	BBDM-1 Epic 1: Emergency Request Management	Medium	To Do	None	None
	BBDM-7 Story 1.1: Submit Emergency Request	High	Done	BBDM-1 Epic 1: Emergency Request Management	5
	BBDM-13 Story 1.2: Urgency Triage	High	Done	BBDM-1 Epic 1: Emergency Request Management	3
	BBDM-16 Story 1.3: Track Request Status	Medium	In Progress	BBDM-1 Epic 1: Emergency Request Management	3
	BBDM-2 Epic 2: Donor Matching & Notification	Medium	To Do	None	None
	BBDM-10 Story 2.1: ABO/Rh Compatibility Check	High	Done	BBDM-2 Epic 2: Donor Matching & Notification	5
	BBDM-11 Story 2.2: Geo-targeted SMS Alerts	High	Done	BBDM-2 Epic 2: Donor Matching & Notification	8
	BBDM-12 Story 2.3: Donor Confirm/Decline	High	Done	BBDM-2 Epic 2: Donor Matching & Notification	5
	BBDM-17 Story 2.4: Radius Expansion & Escalation	Medium	To Do	BBDM-2 Epic 2: Donor Matching & Notification	8
	BBDM-3 Epic 3: Blood Inventory Management	Medium	To Do	None	None
	BBDM-5 Story 3.1: Update Stock	High	Done	BBDM-3 Epic 3: Blood Inventory Management	3
	BBDM-8 Story 3.2: Real-time Availability Check	High	Done	BBDM-3 Epic 3: Blood Inventory Management	5
	BBDM-9 Story 3.4: Prevent Double Allocation	High	Done	BBDM-3 Epic 3: Blood Inventory Management	5
	BBDM-15 Story 3.3: Expiry Flags	Medium	Done	BBDM-3 Epic 3: Blood Inventory Management	3
	BBDM-4 Epic 4: Donor Profile & Data Privacy	Medium	To Do	None	None
	BBDM-6 Story 4.1: Register/Update Donor Profile	High	Done	BBDM-4 Epic 4: Donor Profile & Data Privacy	3
	BBDM-14 Story 4.2: Encrypt Donor Data	High	Done	BBDM-4 Epic 4: Donor Profile & Data Privacy	5
	BBDM-18 Story 4.3: Donation Eligibility Tracking	Low	To Do	BBDM-4 Epic 4: Donor Profile & Data Privacy	2

Figure 4: Story point assignments, priority, status and parent Epic for all User Stories (total 63 points)

3. Burndown Charts

Sprints 2 and 3 were set up with their stories committed before the sprint started, so their charts start at the planned total. Sprint 1's chart is not shown: its six stories were added after the sprint had started, so Jira logged it as starting at 0 points and recorded all 26 points as scope added. That chart jumps from 0 to 26 and back to 0 within minutes, which is an artefact of the simulation.

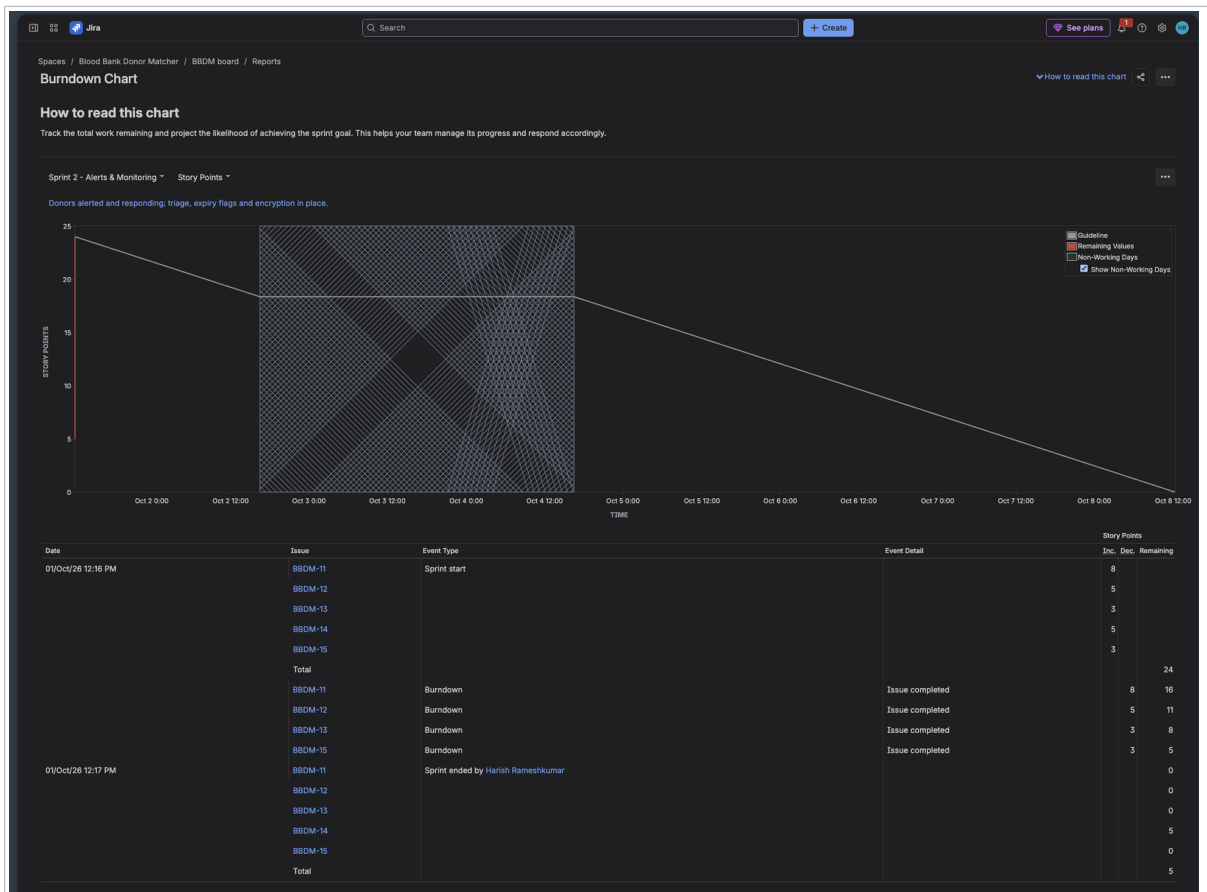


Figure 5: Sprint 2 burndown: 24 points committed, 19 completed, 5 carried over (Story 4.2)

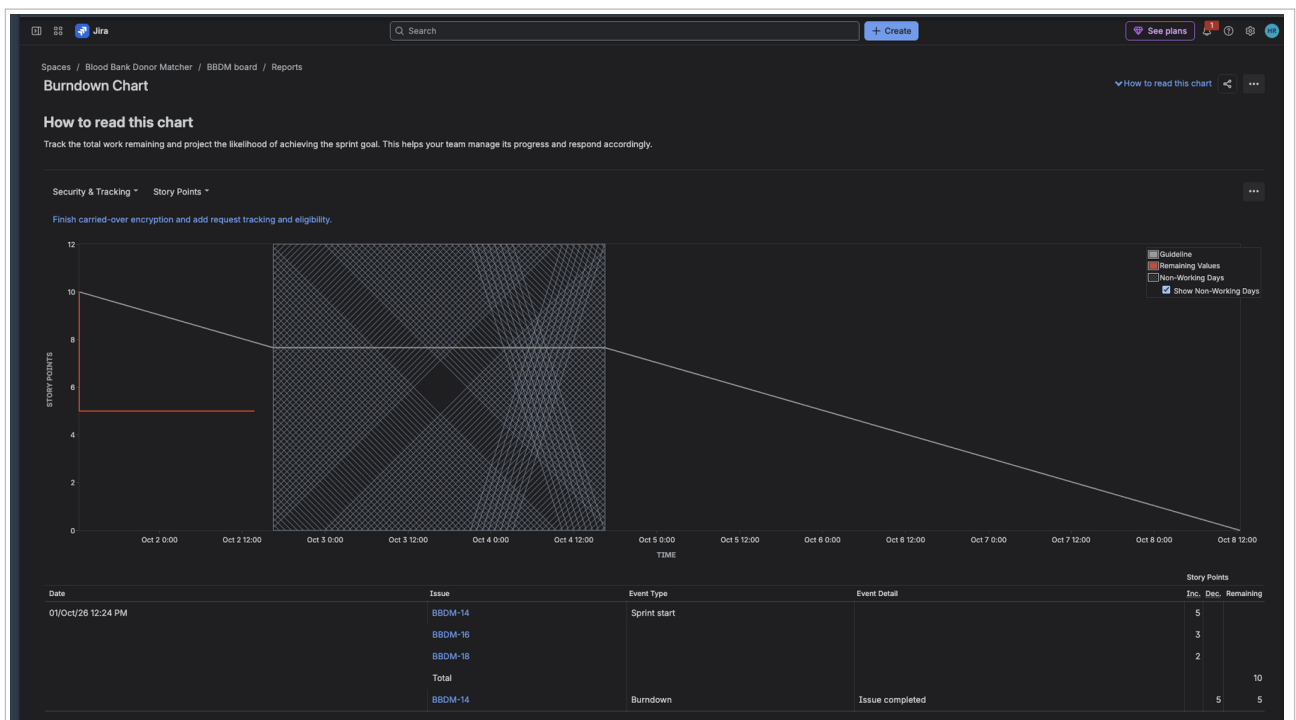


Figure 6: Sprint 3 burndown: 10 points committed, stepping down to 5 after Story 4.2 was completed

4. Sprint Board Outcome

The stories were moved from To Do to In Progress to Done on the Active sprints board. Sprint 3 is still running, so its board is shown live (Figure 7): Story 4.2 is Done, Story 1.3 is In Progress and Story 4.3 is in To Do. Sprints 1 and 2 were completed, so Sprint 2's outcome is shown through Jira's sprint report (Figure 8).

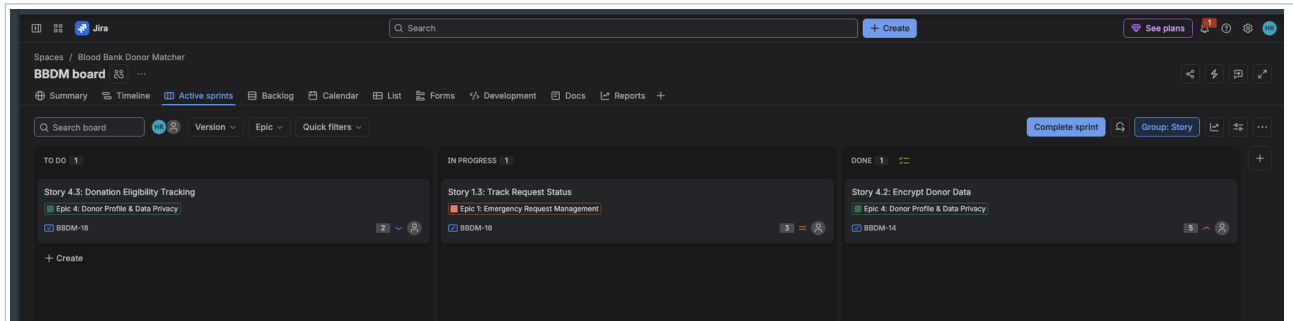


Figure 7: Active sprints board for Sprint 3 with cards in To Do, In Progress and Done

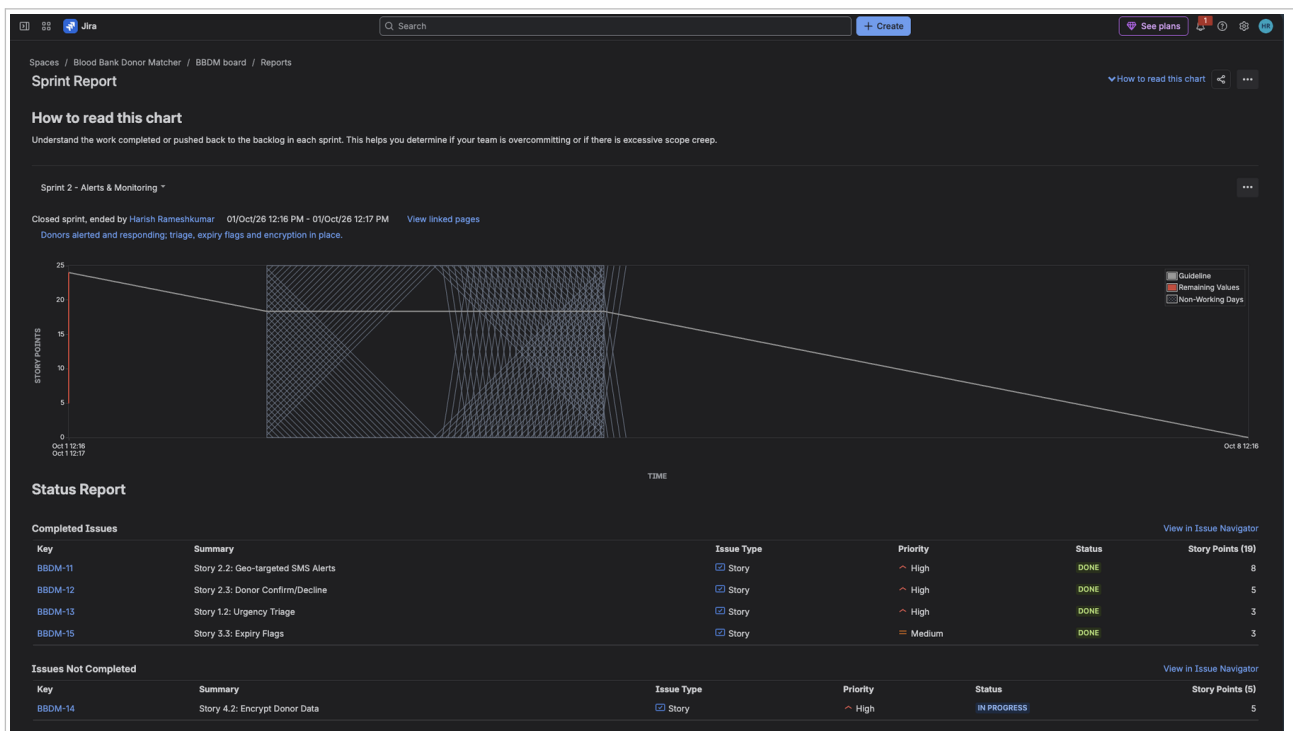


Figure 8: Sprint 2 sprint report: 19 points completed, Story 4.2 (5 points) not completed

5. Reflection

My Jira project broke the system into 4 epics and 14 user stories worth 63 story points, estimated with Fibonacci values (2, 3, 5, 8). I ran three one-week sprints: Sprint 1 and Sprint 2 were completed (45 of 50 planned points) and Sprint 3 is still running.

5.1 Did my estimations reflect the actual effort?

Partly. Sprint 1 completed all 26 points, so those estimates were reasonable or slightly conservative. Sprint 2 completed 19 of 24 points, and the unfinished story was the 5-point encryption story (4.2), which suggests security work carried more uncertainty than I estimated. Sprint 3 then finished 4.2 straight away, so the estimate itself was fair and the story simply needed more time than Sprint 2 gave it. Because this was a simulation, the estimates were tested against my own choices rather than real hours.

5.2 Was my backlog well-prioritised?

Mostly. The foundation stories (stock updates, donor profiles, request intake, availability check, double-allocation lock and compatibility check) went into Sprint 1, so the core flow existed before alerts and notifications were built. One weakness is that 10 of 14 stories were marked High, which weakens the signal that priority is meant to give. Encryption (4.2) was also High but slipped to Sprint 3, so it could have been scheduled earlier or split into smaller pieces.

5.3 How did my simulated sprints align with my plan?

Sprint 1 (Foundation) matched the plan exactly: six stories planned and six completed. Sprint 2 (Alerts & Monitoring) deviated deliberately, with four of five stories finished and Story 4.2 left in progress and moved back to the backlog. Sprint 3 (Security & Tracking) was planned around that carry-over: 4.2 plus two small stories for 10 points. Story 2.4 remains in the backlog by design. All sprints were run in minutes rather than a week, so the timing is compressed compared with a real sprint.

5.4 What insights did the burndown chart give about my team's capacity?

Sprint 2's remaining work fell from 24 to 5 within about a minute and then the sprint ended, showing that work was updated in bulk rather than daily; the 5 points left over were the carried-over Story 4.2. Sprint 3 started correctly at 10 points and stepped down to 5 when 4.2 was done. Velocity was 26 points in Sprint 1 and 19 in Sprint 2, an average of 22.5, so planning 24 points was slightly optimistic. Sprint 1's distorted chart showed that burndown accuracy depends on committing scope before the sprint starts, a lesson applied to Sprints 2 and 3. An important caveat is that the charts reflect simulated rather than real timing, so they show planning and completion totals but not real pacing.

Takeaways

I would commit about 20 to 22 points per sprint, give security stories a larger estimate or split them, use High priority more sparingly, and always commit the full sprint scope before starting a sprint.
