

LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Problem Statement #12: Blood Bank Inventory & Emergency Donor Matcher

Student

Dabbugunta Venya Anand

SRN

PES1UG24AM074

Final Deliverables Included

- Jira backlog showing Epics, User Stories, priorities, and story point estimates
- Active Sprint board showing Sprint 1 work items
- Sprint 1 Burndown Chart
- Sprint reflection answering the four required questions

Project execution summary: 2 Epics, 5 User Stories, 26 total story points, 2 completed sprints.

1. Backlog: Epics, User Stories & Story Points

Evidence of backlog creation, Epic grouping, and Fibonacci-style story point estimation.

The screenshot displays the Jira interface for the 'BBIEDM board' (Blood_Bank_Inventory_Emergency_Donor_Matcher). The 'Backlog' tab is selected, showing a list of work items grouped under two epics: 'Emergency Blood Request & Donor Matching' and 'Blood Inventory Management'. The 'Blood Inventory Management' epic is highlighted with a blue box. The backlog contains five work items, each with a checkbox, ID, title, epic link, status, priority, story points, and assignee. The story points are 5, 5, 8, 3, and 5, respectively, demonstrating Fibonacci-style estimation.

Spaces / Blood_Bank_Inventory_Emergency_Donor_Matcher

BBIEDM board ...

Summary ... Timeline Active sprints **Backlog** Calendar List Forms Development Docs +

Search backlog Version Epic 2 Quick filters Clear filters

Epic X

No epic

Emergency Blood Request & Donor Matching ...

Blood Inventory Management ...

+ Create epic

0 of 0 work items visible Estimate: 0 of 0

☐ **Backlog** (5 work items) 26 0 0 Create sprint

Create a whiteboard to plan your work Try ... X

☒	BBIEDM-3	Submit Emergency Blood Request	Emergency...	To Do	5	^	👤
☒	BBIEDM-4	Verify Blood Compatibility	Emergency...	To Do	5	^	👤
☒	BBIEDM-5	Match Inventory and Notify Donors	Emergency...	To Do	8	^	👤
☒	BBIEDM-6	Update Blood Inventory	Blood Inv...	To Do	3	^	👤
☒	BBIEDM-7	Flag Expiring Blood Units	Blood Inv...	To Do	5	=	👤

+ Create

2. Active Sprint Board - Sprint 1

Sprint 1 contains the selected core stories and is shown in the active sprint workflow.

Spaces / Blood_Bank_Inventory_Emergency_Donor_Matcher

BBIEDM board

Summary Timeline **Active sprints** Backlog Calendar List Forms Development Docs +

Search board Version Epic Quick filters Complete sprint Group: Story

TO DO 3

- Submit Emergency Blood Request**
Emergency Blood Request & Donor Matching
BBIEDM-3 5
- Verify Blood Compatibility**
Emergency Blood Request & Donor Matching
BBIEDM-4 5
- Update Blood Inventory**
Blood Inventory Management
BBIEDM-6 3

+ Create


IN PROGRESS

DONE

Page 3

3. Sprint 1 Burndown Chart

The chart captures simulated progress after 10 of 13 story points were completed, with 3 points remaining.

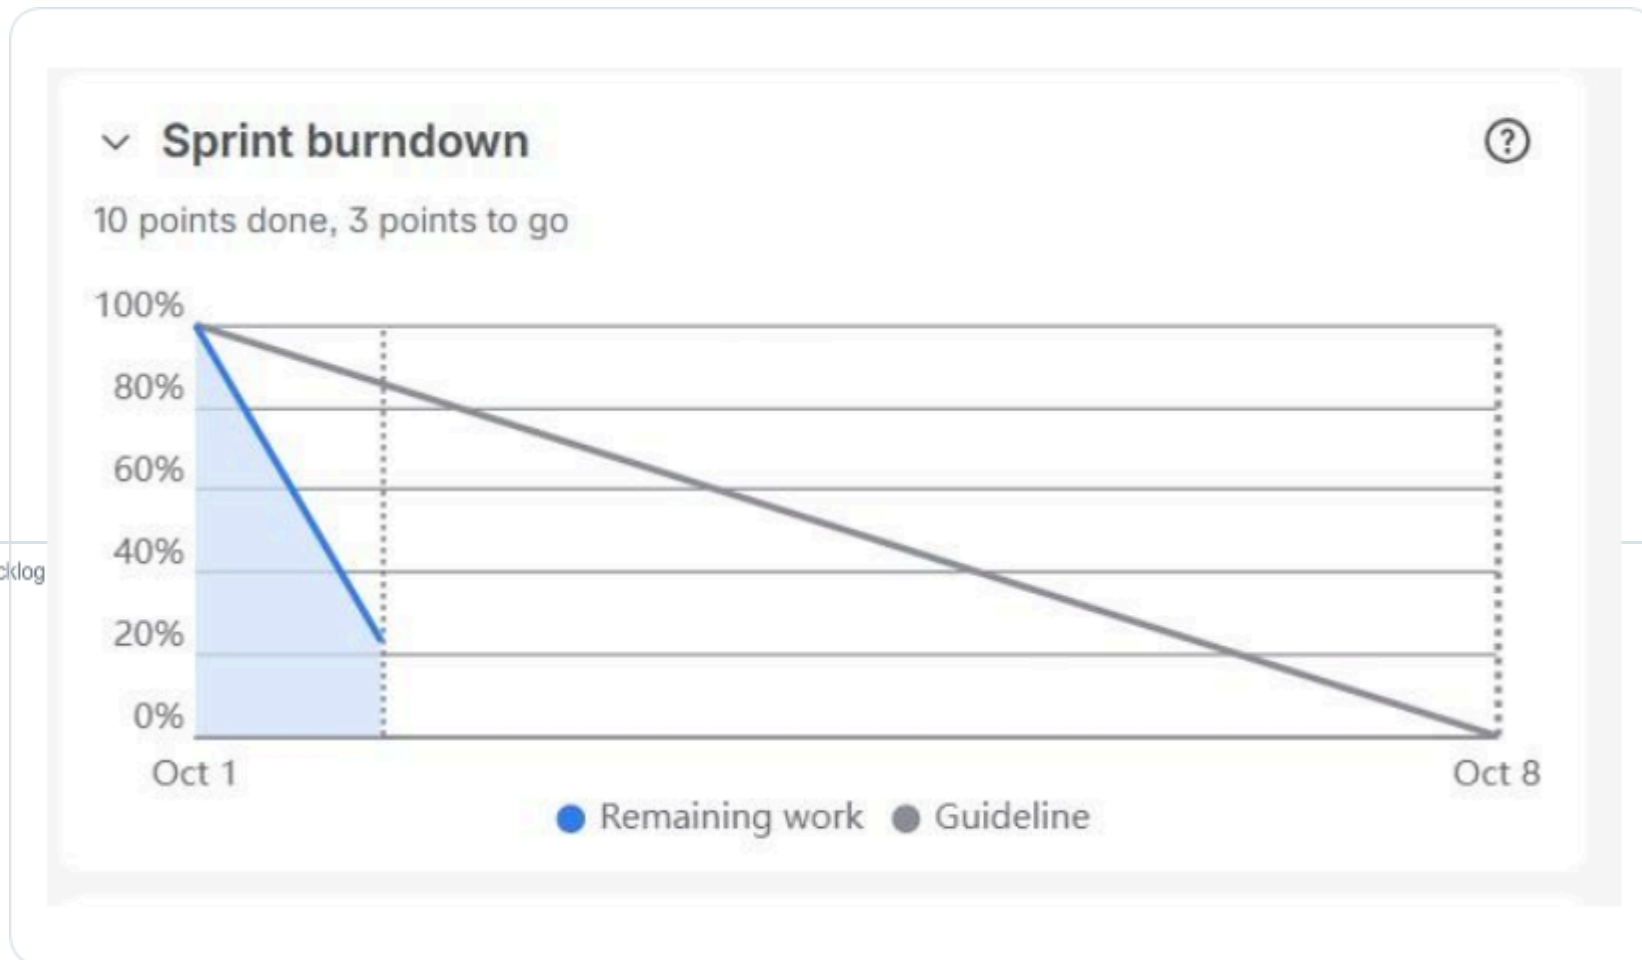

Observation: remaining work falls faster than the grey guideline in this simulation.

4. Sprint Reflection

1. Did the estimations reflect the actual effort?

The story point estimates were reasonable as relative measures of complexity. Simpler inventory updates were assigned fewer points, while the donor matching and notification workflow received the highest estimate because it involved multiple interacting steps. Since the sprint was simulated rather than implemented in real development time, the estimates mainly represented expected complexity rather than measured effort.

2. Was the backlog well-prioritized?

Yes. High-priority emergency functions such as submitting blood requests, verifying compatibility, updating inventory, and matching donors were given priority over the medium-priority expiry-alert feature. This ensured that the most critical blood-bank operations were addressed first.

3. How did the simulated sprint align with the plan?

Sprint 1 contained 13 story points and focused on the core request, compatibility, and inventory workflow. Sprint 2 contained the remaining 13 points and completed donor notification and expiry monitoring. The work items were moved through To Do, In Progress, and Done as planned, and both sprints were completed successfully.

Lab 2 - Agile Backlog Creation & Sprint Simulation in Jira

4. What insights did the burndown chart give about team capacity?

The Sprint 1 burndown showed that 10 of 13 story points were completed while 3 points remained. The remaining-work line dropped faster than the guideline, indicating that work was being completed ahead of the planned rate in the simulation. In a real project, this chart would help the team judge whether its sprint capacity and future commitments are realistic.
